INDIANA STRATEGIC SITES INVENTORY (SSI) PROGRAM


Seven years of statewide site readiness at a glance

What IEDC and the Indiana Power Partners built from 2018 to 2026: the most comprehensive greenfield site inventory of any state, searched in every county and vetted with local officials.

SSI PROGRAM
INDIANA ECONOMIC DEVELOPMENT CORPORATION
Strategic Sites Inventory · 2018 to 2026

92	1,811	235,402	74	490	70	85%
counties searched, both statewide passes	greenfield sites identified	acres identified	county review workshops held	sites ranked 4.0 or higher	potential mega sites, 500 to 5,200 acres	of sites never before listed in ZoomProspector


SCALE: EVERY COUNTY, LOCALLY VETTED

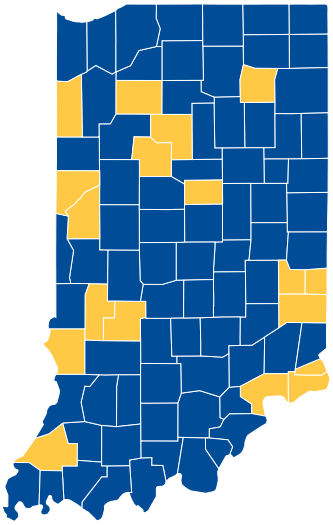

74 counties reviewed and ranked · 18 awaiting review

Phase I searched all 92 counties by project land use: Megasite, Heavy and Light Industrial, Agribusiness, Technology MegaSite, Solar, Data Center. Workshops with county officials ranked 1,385 sites on a 1.0 to 5.0 readiness scale.

THE PIPELINE: IDENTIFIED, RANKED, NOT YET GRADUATED



What graduation means. A site graduates when it has a favorable Phase II opinion, a site visit, a landowner purchase option at fair market value, zoning alignment, and a marketing package, and is then published to the state sites database. Indiana funded the discovery and ranking phases; Phase II was utility-funded on 9 sites, and Phase III site advancement was never started.

TIMELINE

2018 — IEDC and Duke Energy launch statewide Phase I

2020 — Phase I complete, 92 counties; 9 SSI Portals live

2021 — 1,724 sites; 23 workshops (first in Dec 2020); Indy Fast Friday

2022 — 69 Tech MegaSites; SSI Day at IMS; LEAP announced


2023 — "Indiana leads nation"; 38 solar sites, 10 GW

2024 — 74 counties reviewed; data center screens; budget exhausted

2025 — Two $25K amendments; last invoice June 20


2026 — Inventory intact; funding lapsed

INVESTMENT: $1.39 MILLION OVER SEVEN YEARS



IEDC total invoiced under three professional services agreements (2018, 2022, 2023), net of a $25,000 in-kind credit. Utilities funded Phase II at $10,000 per site and their own portal licenses. Since 2022 Ohio has awarded about $350 million to 11 sites (before cutting its fund in 2025) plus $250 million through JobsOhio, and Michigan more than $460 million, to site readiness.

IEDC FUNDING BY YEAR, IN THOUSANDS



Phase I discovery, specialty screens, workshops	$562K
Program management, RFI, technical support	$324K
SSI Portal licensing (IEDC, LEDOs, utilities)	$261K
Site Profiles, NAICS brochures	$134K
Phase II due diligence (utilities)	$130K

PRODUCTS AND DELIVERABLES IN IEDC'S HANDS TODAY

Phase I Site Discovery
All 92 counties, two statewide passes, 1,811 sites, 235,402 acres

Local Site Review Workshops
74 counties; 1,385 sites ranked with county officials

Technology MegaSite search
69 sites of 500 to 5,200 acres in 26 counties (2022)

SSI: Solar Phase I
38 sites, 65,433 acres, 10,142 MW (2023)

SSI: Data Center screens
58 statewide hyperscale candidates; 38 in NIPSCO territory

Phase II due diligence
10 reports complete, 24 nominated, funded by utilities

SSI Portal
9 Indiana instances; IEDC, 8 utilities, 107 LEDO and REDO users

Technical marketing
17 Site Profiles, 6 XCEL profiles, NAICS brochures, RFI support

PARTNERS WHO BUILT IT AND USE IT

Indiana Economic Development Corporation · Duke Energy Indiana · Wabash Valley Power Alliance · NIPSCO · Hoosier Energy · AES Indiana · CenterPoint Energy · Indiana Michigan Power · IMPA · 92 county LEDOs · 15 regional EDOs · Indiana Economic Development Association · Evansville Regional Economic Partnership

Duke Energy Indiana originated the program through a Duke Energy Foundation grant to IEDC in 2018 and has licensed its SSI Portal every year since. NIPSCO built an SSI Phase II Site Preparedness Grant Program on the model; Wabash Valley funded six Phase II studies and a workshop incentive. IEDC markets the LEAP Research and Innovation District as sitting "all on an SSI-certified (Strategic Site Inventory) site."

LOCATION Design Group · SSI PROGRAM

SSI Program conducted by Leotta Location and Design, LLC, now Location Design Group, LLC, an ATK Energy Group Company. Strategic Sites Inventory and SSI are marks of Location Design Group, LLC.

Sources: IEDC contracts, Leotta Location and Design (LL+D)/LDG proposals and invoices 2018 to 2025; IEDC SSI web page (Nov 2026); IEDC releases Nov 2022 and May 2023; companion Program Chronicle. Prepared November 2026.
